



NAPIT



07944 437459

Electrical Installation Condition Report

Requirements for Electrical Installations - BS 7671:2018+A2:2022 as amended
(IET Wiring Regulations 18th Edition)

Guidance for recipients:

This report is an important and valuable document which should be retained for future reference.

1. The purpose of this Report is to confirm, so far as reasonably practicable, whether or not the electrical installation is in a satisfactory condition for continued service (see Section E). The Report should identify any damage, deterioration, defects and/or conditions which may give rise to danger (see Section K).
2. This Report is only valid if accompanied by the Inspection Schedule(s) and the Schedule(s) of Circuit Details and Test Results.
3. The person ordering the Report should have received the original Report and the inspector should have retained a duplicate.
4. The original Report should be retained in a safe place and be made available to any person inspecting or undertaking work on the electrical installation in the future. If the property is vacated, this Report will provide the new owner / occupier with details of the condition of the electrical installation at the time the Report was issued.
5. Section D (Extent and Limitations) should identify fully the extent of the installation covered by this Report and any limitations on the inspection and testing. The inspector should have agreed these aspects with the person ordering the Report and with other interested parties (licensing authority, insurance company, mortgage provider and the like) before the inspection was carried out.
6. Some operational limitations such as inability to gain access to parts of the installation or an item of equipment may have been encountered during the inspection. The inspector should have noted these in Section D.
7. For items classified in Section K as **C1 ("Danger Present")**, the safety of those using the installation is at risk, and it is recommended that a skilled person or persons competent in electrical installation work undertakes the necessary remedial work immediately.
8. For items classified in Section K as **C2 ("Potentially Dangerous")**, the safety of those using the installation may be at risk and it is recommended that a skilled person or persons competent in electrical installation work undertakes the necessary remedial work as a matter of urgency.
9. Where it has been stated in Section K that an observation requires further investigation **code FI** the inspection has revealed an apparent deficiency which may result in a code C1 or C2 could not, due to the extent or limitations of this inspection, be fully identified. Such observations should be investigated as soon as possible. A further examination of the installation will be necessary, to determine the nature and extent of the apparent deficiency (see Section F).
10. **For safety reasons**, the electrical installation should be re-inspected at appropriate intervals by a skilled person or persons competent in such work. The recommended date by which the next inspection is due is stated in Section F of the Report under 'Recommendations' and on a label at or near to the consumer unit /distribution board (where required).
11. Where the installation includes a residual current device (RCD) it should be tested six-monthly by pressing the button marked 'T' or 'Test'. The device should switch off the supply and should then be switched on to restore the supply. If the device does not switch off the supply when the button is pressed, seek expert advice. **For safety reasons it is important that this instruction is followed.**
12. Where the installation includes an arc fault detection device (AFDD) having a manual test facility it should be tested six-monthly by pressing the test button. Where an AFDD has both a test button and automatic test function, manufacturer's instructions shall be followed with respect to test button operation.
13. Where the installation includes a surge protective device (SPD) the status indicator should be checked to confirm it is in operational condition in accordance with manufacturer's information. If the indication shows that the device is not operational, seek expert advice. For safety reasons it is important that this instruction is followed.
14. Where the installation includes alternative or additional sources of supply, warning notices should be found at the origin or meter position or, if remote from the origin, at the consumer unit or distribution board and at all points of isolation of all sources of supply.

ELECTRICAL INSTALLATION CONDITION REPORT

FT/EICR

768900003779

for Residential or Similar Premises up to 100 A

Requirements for Electrical Installations
BS 7671:2018+A2:2022 as amended
(IET Wiring Regulations 18th Edition)

NAPIT



07944 437459

A. Details of the Installation

Client	Opago	Installation	
Address	10 Cromwell Place South Kensington LONDON	Address	Flat 3 ,3 Queen's Gate Place LONDON
Postcode	SW7 2JN	Postcode	SW7 5NT

B. Reason for Producing this Report

This form is to be used only for reporting on the condition of an existing installation.

Essential information requested by client in accordance with the EAWR 1989. Testing of the fixed wiring of the installation to establish --Please see Continuation Page--

Date(s) on which the inspection and testing were carried out to

C. Details of Installation which is the Subject of this Report

Description of premises Residential or Similar Commercial Industrial Other (please specify)

Estimated age of the wiring system years

Evidence of alterations or addition Yes No Not apparent if 'Yes', estimated years

Records of installation available Yes No Records held by

Date of last inspection Electrical Installation Certificate No. or previous Inspection Report No.

D. Extent of Electrical Installation Covered by this Report:

The Sample Inspection of the Installation was made in accordance with Guidance Notes 3, Table 3.3 and 3.4. Consumer Unit external Inspection 100%. Consumer Unit internal Inspection - Because It was possible to isolate the consumer unit during the EICR, the electrical connections within the consumer were checked (torqued) against the manufacturer's specifications. Final circuits - every final circuit was inspected where accessible how-ever, there was no access to --Please see Continuation Page--

Agreed Limitations and Operational Limitations (Regulations 653.2)

Cables concealed under floors, above ceilings or in walls/partitions, adequately protected against damage (see Section D. Extent and limitations) & (522.6.204). Some of the accessories not accessible due to heavy furniture or equipment in place. No access to main cut out, distribution equipment .
--Please see Continuation Page--

Agreed with: Extent of Termination Sampling: The inspection and testing detailed within this report and accompanying schedule has been carried out in accordance with BS 7671: 2018 (IET Wiring Regulations) amended to

It should be noted that cables concealed within trunkings and conduits, under floors, in roof spaces and generally within the fabric of the building or underground have NOT been inspected unless specifically agreed between the client and inspector prior to the inspection. An inspection should be made within an accessible roof space housing other electrical equipment.

E. Summary of the Condition of the Installation

Overall assessment of the installation in terms of its suitability for continued use

SATISFACTORY *UNSATISFACTORY

General conditions of the installation (in terms of electrical safety)

Non SPD with combinations of RCDs & RCBOs / additional protection on plastic body consumer unit. Ze, Zs readings and RCD / RCBO tripping time comply with current regulation. All outgoing circuits protected via 30mA RCD. Hard wire smoke & heat detectors been installed / tested.

*An UNSATISFACTORY assessment indicates that dangerous (code C1), or potentially dangerous (code C2) conditions have been identified

F. Recommendations

Where the overall assessment of the suitability of the installation for continued use above is stated as UNSATISFACTORY I/we recommend that any observations classified as 'Danger present' (code C1) or 'Potential dangerous' (code C2) are acted upon as a matter of urgency. Investigation without delay is recommended for observations identified as 'Further Investigation required' (code F1). Observations classified as 'Improvement recommended' (code C3) should be given due consideration. Subject to the necessary remedial action being taken, I/we recommend that the installation is further inspected and tested by (date) for the following reasons:

3 years to next inspection in line with the Private Rented Sector 2020 Regulations.

G. Declaration

I/we being the person(s) responsible for the inspection and testing of the electrical installation (as indicated by my/our signatures below), particulars of which are described above, having exercised reasonable skill and care when carrying out the inspection and testing hereby declare that the information in this report, including the observations and the attached schedules, provides an accurate assessment of the condition of the electrical installation taking into account the stated extent and limitations in section D of this report.

Company	Dave Electrical Services Tel:07944 437459	Inspected and tested by	Authorised for issue by
Address	7 Nursery Gardens, Hounslow,	Name:	Vaibhav Dave
Postcode	TW4 5EY	Signature:	Vaibhav Dave
Branch No.	N/A	Position:	Installer/Inspector
Scheme No.	30178	Date:	23/07/2025

H. Schedule(s)

schedule(s) of inspection and schedule(s) of Circuit Details and Test Results are attached.

The attached schedule(s) are part of this document and this report is valid only when they are attached to it.

ELECTRICAL INSTALLATION CONDITION REPORT

FT/EICR

768900003779

for Residential or Similar Premises up to 100 A

Requirements for Electrical Installations
BS 7671:2018+A2:2022 as amended
(IET Wiring Regulations 18th Edition)



NAPIT



07944 437459

I. Supply Characteristics and Earthing Arrangements

Earthing Arrangements TN-S TN-C-S TT Other Please specify LIM

Number & Type of live conductors AC DC No. of phases 1 No. of wires 2

Nature of Supply Parameters (Note: ⁽¹⁾ by enquiry, ⁽²⁾ by enquiry or by measurement)

Nominal voltage, U/U₀ ⁽¹⁾ 230 v Nominal frequency, f⁽¹⁾ 50 Hz Confirmation of supply polarity

Prospective fault current, I_{pf} ⁽²⁾ 1.1 kA External loop impedance, Z_e ⁽²⁾ 0.22 Ω

Supply Protective Device BS (EN) LIM Type LIM Rated Current LIM A

No. of Additional Supplies N/A

J. Particulars of Installation Referred to in this Report

Details of installation Earth Electrode (where applicable) Type (e.g. rod(s), tape etc) N/A Distributors facility Installation Earth Electrode

Location N/A Electrode resistance to earth N/A Ω Maximum Demand (load) 44 Amps KVA

Main Protective Conductors	Material	csa	(✓) or Value	(✓) or Value
Earthing Conductor	Copper	16 mm ²	Continuity Verified <input type="checkbox"/>	Connection Verified <input checked="" type="checkbox"/>
Protective Bonding Conductor	Copper	10 mm ²	Continuity Verified <input checked="" type="checkbox"/> 0.03 Ω	Connection Verified <input checked="" type="checkbox"/> 0.02 Ω

Main Supply Conductor	Material	csa	(connection / continuity) (✓) or Value	(✓) or Value
	Copper	16 mm ²	Water installation <input checked="" type="checkbox"/>	To structural steel NA <input type="checkbox"/>
Main Switch Location	LIM		Gas installation pipes NA <input type="checkbox"/>	To lightning protection NA <input type="checkbox"/>
Fuse/device rating or setting	LIM A	Voltage rating LIM V	Oil installation pipes NA <input type="checkbox"/>	Other <input type="checkbox"/>

If RCD main switch: Rated residual operating current I_{Δn} LIM mA

BS(EN) LIM No. of Poles LIM Current Rating LIM A Rated time delay LIM ms Measured operating trip time ms

K. Observations

Referring to the attached inspection schedule(s) and schedule(s) of circuit details and test results, and subject to the limitations specified at the Extent and limitations of inspection and testing Section D.

No remedial work required

The following observations are made

Item No.	Observation	Code
1	DB - : 3.8 Accessibility and condition of other protective bonding connections (543.3.1; 543.3.2) - Supplementary bonding connection is not accessible	C3
2	DB - : 4.18 RCD(s) provided for additional protection/requirements - includes RCBO(s) (411.3.3; 415.1) - Type AC RCD is supplying multiple outlets and not fixed equipment, where there are no DC leakage components present	C3
3	DB - : 4.4 Condition of enclosure(s) in terms of fire rating etc (421.1.201; 526.5) - CU in a domestic household premises is not metal or installed in a non-combustible cabinet, showing No signs of thermal damage, located under a wooden or combustible public stairwell forming part of an escape route from a dwelling area	C3
4	DB - : 3.7 Condition and accessibility of main protective bonding conductor connections (543.3.2; 544.1.2) - Main protective bonding connection is not accessible.	C3
5	DB - : 4.13 Compatibility of protective devices, bases and other components; correct type and rating, (No signs of unacceptable thermal damage, arcing or overheating) (411.4; 411.5; 411.6; Sections 432,433) - No SPD protection for cables traversing the external/internal zones 0/1 (telephone lines, TV coax, external circuits on the ground and from roof mounted plant, etc.) No LPS fitted	C3
6	DB - : 4.4 Condition of enclosure(s) in terms of fire rating etc (421.1.201; 526.5) - The CU has excessive hole in the rear of the enclosure fixed to flammable surface and has No signs of thermal damage	C3

One of the following codes, as appropriate, has been allocated to each of the observations made above and/or any attached observation sheets to indicate to the person(s) responsible for the installation the degree of urgency for remedial action.

C1 Danger present. Risk of Injury. Immediate remedial action required.	
C2 Potentially dangerous. Urgent remedial action required.	
C3 Improvement recommended.	1, 2, 3, 4, 5, 6
FI Further Investigation required without delay	

for Residential or Similar Premises up to 100 A

Requirements for Electrical Installations
BS7671:2018+A2:2022 as amended (IET Wiring Regulations 18th Edition)



07944 437459

Outcomes

Acceptable condition:	Unacceptable condition: State	Improvement recommended:	Further Investigation:	Not Verified:	Limitation:	Not Applicable:	Inadequacies: (Items 1.1 - 1.1.5 Only)
	or						

In the outcome column use the codes above. Provide additional comment where appropriate. C1/C2/C3 and FI coded items to be recorded in section K of the condition report.

Item No.	Description	Outcome
1.0 INTAKE EQUIPMENT (VISUAL INSPECTION ONLY);		
1.1	Service cable	
1.1.1	Service head	
1.1.2	Earthing arrangement	
1.1.3	Meter tails	
1.1.4	Metering equipment	
1.1.5	Isolator (where present)	
1.1.6	Person ordering work/dutyholder notified NOTE 1 Where inadequacies in the intake equipment are encountered, which may result in a dangerous or potentially dangerous situation, the person ordering the work and/or dutyholder must be informed. It is strongly recommended that the person ordering the work informs the appropriate authority. NOTE 2 For this section only, where inadequacies are found, an X should be put against the appropriate item and a comment made in Section K	
1.2	Consumer's Isolator (where present)	
1.3	Consumer's meter tails	
2.0 Presence of adequate arrangements for other sources such as microgenerators (551.6; 551.7)		
2.1	Presence of adequate arrangements where generator to operate as a switched alternative (551.6)	
2.2	Adequate arrangements where a generating set operates in parallel with the public supply (551.7)	
3.0 EARTHING / BONDING ARRANGEMENTS (411.3; Chap 54)		
3.1	Presence and condition of distributor's earthing arrangements (542.1.2.1: 542.1.2.2)	
3.2	Presence and condition of earth electrode connection where applicable (542.1.2.3)	
3.3	Provision of earthing/bonding labels at all appropriate locations (514.13.1)	
3.4	Confirmation of earthing conductor size (542.3; 543.1.1)	
3.5	Accessibility and condition of earthing conductor at MET arrangement (543.3.2)	
3.6	Confirmation of main protective bonding conductor sizes (544.1)	
3.7	Condition and accessibility of main protective bonding conductor connections (543.3.2; 544.1.2)	
3.8	Accessibility and condition of other protective bonding connections (543.3.1: 543.3.2)	
4.0 CONSUMER UNIT(S) / DISTRIBUTION BOARD(S)		
4.1	Adequacy of working space/accessibility to consumer unit/distribution board (132.12; 513.1)	
4.2	Security of fixing (134.1.1)	
4.3	Condition of enclosure(s) in terms of IP rating etc (416.2)	
4.4	Condition of enclosure(s) in terms of fire rating etc (421.1.201; 526.5)	
4.5	Enclosure not damaged/deteriorated so as to impair safety (651.2)	
4.6	Presence of main linked switch (as required by 462.1.201)	
4.7	Operation of main switch(es) (functional check) (643.10)	
4.8	Manual operation of circuit-breakers and RCDs and AFDDs to prove functionality (643.10)	
4.9	Correct identification of circuit details and protective devices (514.8.1; 514.9.1)	
4.10	Presence of RCD six-monthly test notice at or near consumer unit/distribution board, where required (514.12.2)	
4.11	Presence of alternative supply warning notice at or near consumer unit/distribution board (514.15)	
4.12	Presence of other required labelling (please specify) (Section 514)	
4.13	Compatibility of protective devices, bases and other components; correct type and rating, (No signs of unacceptable thermal damage, arcing or overheating) (411.4; 411.5; 411.6; Sections 432,433)	
4.14	Single-pole switching or protective devices in line conductor only (132.14.1; 530.3.3)	
4.15	Protection against mechanical damage where cables enter consumer unit/distribution board (522.8.1; 522.8.5; 522.8.11)	
4.16	Protection against electromagnetic effects where cables enter consumer unit/distribution board/enclosures (521.5.1)	
4.17	RCD(s) provided for fault protection -includes RCBO(s) (411.4.204; 411.5.2; 531.2)	
4.18	RCD(s) provided for additional protection/requirements - includes RCBO(s) (411.3.3; 415.1)	
4.19	Confirmation of indication that SPD is functional (651.4)	
4.20	Confirmation that ALL conductor connections, including connections to busbars, are correctly located in terminals and are tight and secure (526.1)	
4.21	Adequate arrangements where a generating set operates as a switched alternative to the public supply (551.6)	
4.22	Adequate arrangements where a generating set operates in parallel with the public supply (551.7)	
5.0 FINAL CIRCUITS		
5.1	Identification of conductors (514.3.1)	
5.2	Cables correctly supported throughout their run (521.10.202; 522.8.5)	
5.3	Condition of insulation of live parts (416.1)	
5.4	Non-sheathed cables protected by enclosure in conduit, ducting or trunking (521.10.1). To include in the integrity of conduit and trunking systems (metallic and plastic)	

for Residential or Similar Premises up to 100 A

Requirements for Electrical Installations
BS7671:2018+A2:2022 as amended (IET Wiring Regulations 18th Edition)



07944 437459

5.5	Adequacy of cables for current-carrying capacity with regard for the type and nature of installation (Section 523)	✓
5.0 FINAL CIRCUITS CONT		
5.6	Coordination between conductors and overload protective devices (433.1; 533.2.1)	✓
5.7	Adequacy of protective devices: type and rated current for fault protection (411.3)	✓
5.8	Presence and adequacy of circuit protective conductors (411.3.1: Section 543)	✓
5.9	Wiring system(s) appropriate for the type and nature of the installation and external influences (Section 522)	✓
5.10	Concealed cables installed in prescribed zones (see Section D. Extent and limitations) (522.6.202)	⚠
5.11	Cables concealed under floors, above ceilings or in walls/partitions, adequately protected against damage (see Section D. Extent and limitations) (522.6.204)	⚠
5.12 PROVISION OF ADDITIONAL REQUIREMENTS FOR RCD NOT EXCEEDING 30 mA:		
5.12.1	For all socket-outlets of rating 32 A or less, unless an exception is permitted (411.3.3)	✓
5.12.2	For the supply of mobile equipment not exceeding 32 A rating for use outdoors (411.3.3)	✓
5.12.3	For cables concealed in walls at a depth of less than 50 mm (522.6.202; 522.6.203)	✓
5.12.4	For cables concealed in walls/partitions containing metal parts regardless of depth (522.6.203)	✓
5.12.5	Final circuits supplying luminaires within domestic (household) premises (411.3.4)	✓
5.12.6	For lighting that is accessible to the public (714.411.3.4)	✓
5.13	Provision of fire barriers, sealing arrangements and protection against thermal effects (Section 527)	✓
5.14	Band II cables segregated/separated from Band I cables (528.1)	✓
5.15	Cables segregated/separated from communications cabling (528.2)	✓
5.16	Cables segregated/separated from non-electrical services (528.3)	✓
5.17 TERMINATION OF CABLES AT ENCLOSURES - INDICATE EXTENT OF SAMPLING IN SECTION D OF THE REPORT (SECTION 526)		
5.17.1	Connections soundly made and under no undue strain (526.6)	✓
5.17.2	No basic insulation of a conductor visible outside enclosure (526.8)	⚠
5.17.3	Connections of live conductors adequately enclosed (526.5)	⚠
5.17.4	Adequately connected at point of entry to enclosure (glands, bushes etc.) (522.8.5)	✓
5.18	Condition of accessories including socket-outlets, switches and joint boxes (651.2 (v))	✓
5.19	Suitability of accessories for external influences (512.2)	✓
5.20	Adequacy of working space/accessibility to equipment (132.12; 513.1)	✓
5.21	Single-pole switching or protective devices in line conductors only (132.14; 530.3.3)	✓
6.0 LOCATION(S) CONTAINING A BATH OR SHOWER		
6.1	Additional protection for all low voltage (LV) circuits by RCD not exceeding 30 mA (701.411.3.3)	✓
6.2	Where used as a protective measure, requirements for SELV or PELV met (701.414.4.5)	✓
6.3	Shaver supply units comply with BS EN 61558-2-5 formerly BS 3535 (701.512.3)	✓
6.4	Presence of supplementary bonding conductors, unless not required by BS 7671:2018 (701.415.2)	✓
6.5	Low voltage (e.g. 230 V) socket-outlets sited at least 2.5 m from zone 1 (701.512.3)	✓
6.6	Suitability of equipment for external influences for installed location in terms of IP rating (701.512.2)	✓
6.7	Suitability of accessories and controlgear etc. for a particular zone (701.512.3)	✓
6.8	Suitability of current-using equipment for particular position within the location (701.55)	✓
7.0 OTHER PART 7 SPECIAL INSTALLATIONS OR LOCATIONS		
7.1	List all other special installations or locations present, if any. (Record separately the results of particular inspections applied.)	N/A
8.0 PROSUMER'S LOW VOLTAGE ELECTRICAL INSTALLATION(S)		
8.1	Where the installation includes additional requirements and recommendations relating to Chapter 82, additional inspection items should be added to the checklist.	N/A

9.0 Schedule of Tests

Results to be recorded on Schedule of Test Results

9.1	External earth loop impedance, Z ^e	Yes
9.2	Installation earth electrode	Yes
9.3	Prospective fault current, I _p ^f	Yes
9.4	Continuity of Earth Conductors	Yes
9.5	Continuity of Circuit Protective Conductors	Yes
9.6	Continuity of ring final circuit	Yes
9.7	Continuity of Protective Bonding Conductors	Yes
9.8	Volt drop verified	Yes

9.9	Insulation Resistance between Live Conductors	Yes
9.10	Insulation Resistance between Live Conductors & Earth	Yes
9.11	Polarity (prior to energisation)	Yes
9.12	Polarity (after energisation) including phase sequence	Yes
9.13	Earth Fault Loop Impedance	Yes
9.14	RCDs/RCBOs including selectivity	Yes
9.15	Functional testing of RCD devices	Yes
9.16	Functional testing of AFDD(s) devices	N/A

Inspector's Name: Vaibhav Dave
Date: 23/07/2025

Signature: *Vaibhav Dave*

ELECTRICAL INSTALLATION CONDITION REPORT - Circuit Details

FT/EICR **768900003779**

for Residential or Similar Premises up to 100 A

Requirements for Electrical Installations
BS7671 :2018+A2:2022 as amended (IET Wiring Regulations 18th Edition)



07944 437459

Client Name	Opago	Installation Address	, Flat 3 ,3 Queen's Gate Place, LONDON
Client Address	10 Cromwell Place, South Kensington LONDON	Postcode	SW7 5NT
Client Postcode	SW7 2JN		

Distribution board details - Complete in every case SPD Details: Type(s)* T1 <input type="checkbox"/> T2 <input type="checkbox"/> T3† <input type="checkbox"/> N/A <input checked="" type="checkbox"/> Location In bathroom <input type="checkbox"/> inside cupboard <input checked="" type="checkbox"/> Designation Hager/ Plastic No. of ways 21		Complete only if the distribution board is not connected directly to the origin of the installation Overcurrent protective device for the distribution circuit: Supply to distribution board is from _____ No. of phases 1 BS(EN) N/A Type N/A Rating N/A A Nominal voltage N/A V RCD BS(EN) 61008 Type AC Rating 30 IΔn mA	
---	--	---	--

SCHEDULE OF CIRCUIT DETAILS

Circuit No. and Line	Circuit designation	Type of wiring	Ref. method ‡	No. of points served	Circuit conductors csa (mm²)		Maximum disconnection time (BS 7671) (S)	Overcurrent protective devices			Breaking capacity (KA)	BS 7671 Max. permitted Zs Other §	RCD				
					L / N	OPC		BS EN Number	Type No.	Rating (A)			BS EN Number	Type No.	IΔn (mA)	Rating (A)	
	Main Switch	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
	Main Switch	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A
1	Oven	A3	101	1	6	2.5	0.4	61009	B	32	6	1.09	61009	AC	30	N/A	
2	Hob	A3	101	1	6	2.5	0.4	61009	B	32	6	1.09	61009	AC	30	N/A	
3	Coffee machine	A3	101	1	6	2.5	0.4	60898	B	32	N/A	1.09	61009	N/A	N/A	N/A	
4	Fridge	A3	101	1	4	1.5	0.4	61009	B	20	6	1.75	61009	AC	30	N/A	
5	Airconditioning	A3	101	1	4	1.5	0.4	61009	B	32	6	1.09	61009	AC	30	N/A	
6	Node	A3	101	1	4	1.5	0.4	61009	B	20	6	1.75	61009	AC	30	N/A	
7	AC Condeser	A3	101	2	10	6	0.4	61009	B	32	6	1.09	61009	AC	30	N/A	
8	Security	A3	101	1	4	1.5	0.4	61009	B	20	6	1.75	61009	AC	30	N/A	
9	Microwave	A3	101	1	4	1.5	0.4	61009	B	16	6	2.18	61009	AC	30	N/A	
10	Boiler	A3	101	1	2.5	1.5	0.4	61009	gG	16	6	1.94	61009	AC	30	N/A	
11	Lights kitchen	A3	101	16	1.5	1	0.4	61009	B	10	6	3.49	61009	AC	30	N/A	
12	Lights bed bath	A3	101	6	1.5	1	0.4	61009	B	10	6	3.49	61009	AC	30	N/A	
13	Smoke alarm	A3	101	4	1.5	1.0	0.4	61009	B	10	6	3.49	61009	AC	30	N/A	
14	Lights	A3	101	24	1.5	1.0	0.4	61009	B	6	6	5.82	61009	AC	30	N/A	
	RCD Module	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	
	RCD Module	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	N/A	
15	Bed hall ring	A3	101	11	2.5	1.5	0.4	60898 MCB	B	32	6	1.09	61008	AC	30	100	
16	Flat ring	A3	101	16	2.5	1.5	0.4	60898 MCB	B	32	6	1.09	61008	AC	30	100	
17	Kitchen ring	A3	101	9	2.5	1.5	0.4	60898 MCB	B	32	6	1.09	61008	AC	30	100	

Wiring Types: **A** PVC/PVC, **B** PVC cables in metallic Conduit, **C** PVC cables in non-metallic Conduit, **D** PVC cables in metallic trunking, **E** PVC cables in non-metallic trunking, **F** PVC/SWA cables, **G** SWA/XPLE cables, **H** Mineral Insulated, **MW** Metal Work, **FM** Ferrous Metal, **O** Other

* SPD Type. Where a combined T1 + T2 or T2 + T3 device is installed, indicate by ticking both boxes.
 † Where a T3 SPD is installed to protect sensitive equipment, enter Details of Circuits, of the Schedule of Test Results. (See Section 534 of BS 7671:2018+A2:2022.)
 ‡: See Table 4A2 of Appendix 4 of BS 7671:2018+A2:2022.
 § Where the maximum permitted earth fault loop impedance value stated in Max Zs column is taken from a source other than the tabulated values given in Chapter 41 of BS 7671:2018+A2:2022, state the source of the data in the appropriate cell for the circuit in the change to Schedule of Test Results

**NAPIT**

07944 437459

Generic Continuation

Reason for Producing this Report:

compliance with BS7671:2018 and identify any non-conformities with the regulations and any potential hazards or safety issues that require attention.

Extent and Limitations of Inspection and Testing:


the electrical circuits / cables or points that are installed behind the kitchen appliances or behind dishwashers/washing machines and other fixed appliances. Final circuit accessories - 1nr of point per circuit was dismantled and inspected. Continuity of protective conductors were tested via earth loop impedance testing, Continuity of bonding conductors tested via the R2 Test procedure. Continuity of the Ring Final Circuits tested by the r1/rn/r2 test procedure, Polarity and Earth faulty loop impedance (Zs) test procedures done, Insulation resistance testing between Live conductors and Earth done at 500v where possible and at 250v for circuits where there is a risk of damaging equipment, Functional tests of the RCD's (if any) and the MCB's and any isolators.

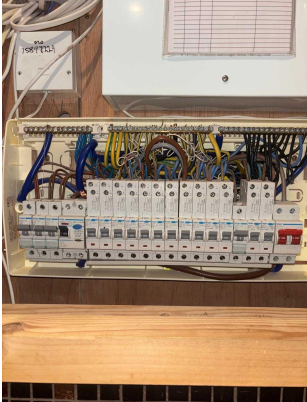
Agreed limitations and operational limitations:

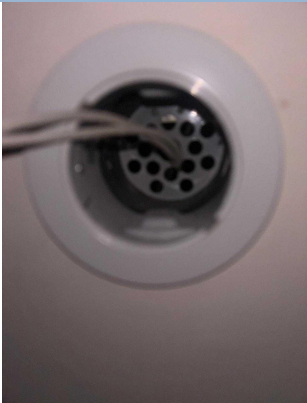
for Residential or Similar Premises up to 100 A



**Requirements for Electrical Installations
BS 7671:2018 (IET Wiring Regulations 18th Edition)**

Item	Photograph of Observation	Observation Details
1		<p>Non SPD with combinations of RCDs & RCBOs / additional protection on plastic body consumer unit.</p> <p>Ze, Zs readings and RCD / RCBO tripping time comply with current regulation.</p> <p>All outgoing circuits protected via 30mA RCD.</p>

Item	Photograph of Observation	Observation Details
2		<p>The CU has excessive hole in the rear of the enclosure fixed to flammable surface and has No signs of thermal damage</p>

Item	Photograph of Observation	Observation Details
3		<p>Fire rated downlights (no access on connections as glued / silicon with ceiling)</p>

for Residential or Similar Premises up to 100 A





NAPIT



07944 437459

Requirements for Electrical Installations
BS 7671:2018 (IET Wiring Regulations 18th Edition)

Item	Photograph of Observation	Observation Details
4		

Item	Photograph of Observation	Observation Details
5		FYI - Smoke detectors running out July 2025
